




# City of Hallandale Beach Public Works Department

## Community Development Block Grant 47<sup>th</sup> Year (CDBG 47) Storm Drainage Improvement Project



The CDBG 47<sup>th</sup> year commenced on January 9, 2023 and completed on June 14, 2023. The project's main focus was to reduce/alleviate flooding issues by installing five (5) catch basins with drainage inlets, and one hundred sixty-four (164) linear feet of hp storm pipe including one hundred forty-one (141) exfiltration trench along NW 10th Street between North Dixie Highway and NW 2nd Avenue. Also, this improvement included asphalt pavement restoration and markings, replacement of 157.45 square yard of sidewalks, new ADA compliant ramps and speed table.

The construction cost for this project is **\$265,690.00.**

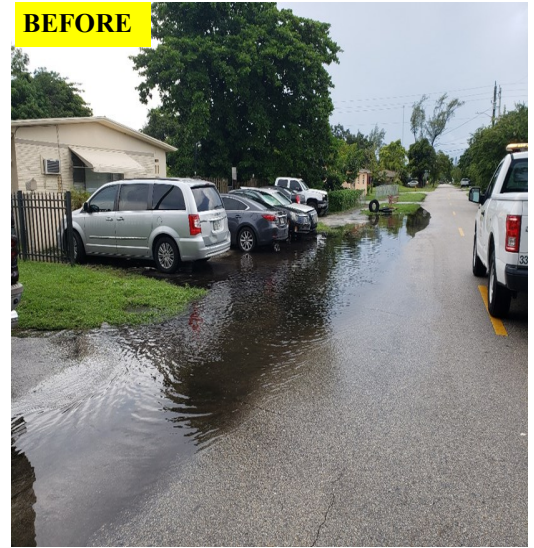

**Project was managed and inspected by: Joselaine Pateau, Project Manager**
